

Project Name **Silver Lake Lead Service Line Replacement**
 Project Manager Colin Gower
 Project Start Date 7/8/2024
 Project Finish Date 10/10/2024
 Duration 69 days
 % complete 0%
 Exported on 6/26/2024



Task number	Critical Items	Name	Start	Finish	Duration
1	1	Mobilize & Set Inlet Protection	7/8/2024	7/9/2024	2 days
2	2 - Athens & Kingston	Lead Service Replacement Area 2 - Athens, Kingston, Orchard, Highland, Markle, Silverlake NE	7/9/2024	8/12/2024	25 days
3	3	Area 2 Hard & Soft Surface Restoration	8/7/2024	8/29/2024	17 days
4	4	Lead Service Replacement Area 1 - Silverlake, Overlook, Ivanhoe	8/13/2024	8/29/2024	13 days
5	5	Area 1 Hard & Soft Surface Restoration	8/26/2024	9/12/2024	14 days
6	6	Lead Service Replacement Area 3 - Millboro, Hastings, Kent, N Park	9/3/2024	9/20/2024	14 days
7	7	Area 3 Hard & Soft Surface Restoration	9/23/2024	10/10/2024	14 days


Untitled map

5 views
Last edit was 6 days ago

Add layer Share Preview

Untitled layer

- 3093 Highland Dr
- 3107 Highland Dr
- 3112 Highland Dr
- 3135 Highland Dr
- 3141 Highland Dr
- 3140 Highland Dr
- 3144 Highland Dr
- 3151 Highland Dr
- 3162 Highland Dr
- 3094 Athens Rd
- 3099 Athens Rd
- 3102 Athens Rd
- 3109 Athens Rd
- 3114 Athens Rd
- 3115 Athens Rd
- 3121 Athens Rd
- 3072 Markle Dr
- 3092 Markle Dr
- 3088 Markle Dr
- 3065 Orchard Rd
- 3070 Orchard Rd
- 3077 Orchard Rd
- 3087 Orchard Rd
- 3096 Orchard Rd
- 3099 Orchard Rd
- 3100 Orchard Rd
- 3035 Kingston Cir
- 3038 Kingston Cir
- 3045 Kingston Cir
- 3051 Kingston Cir
- 3055 Kingston Cir
- 3056 Kingston Cir
- 3060 Kingston Cir
- 3059 Kingston Cir
- 3038 Endicott Way
- 3057 Endicott Way

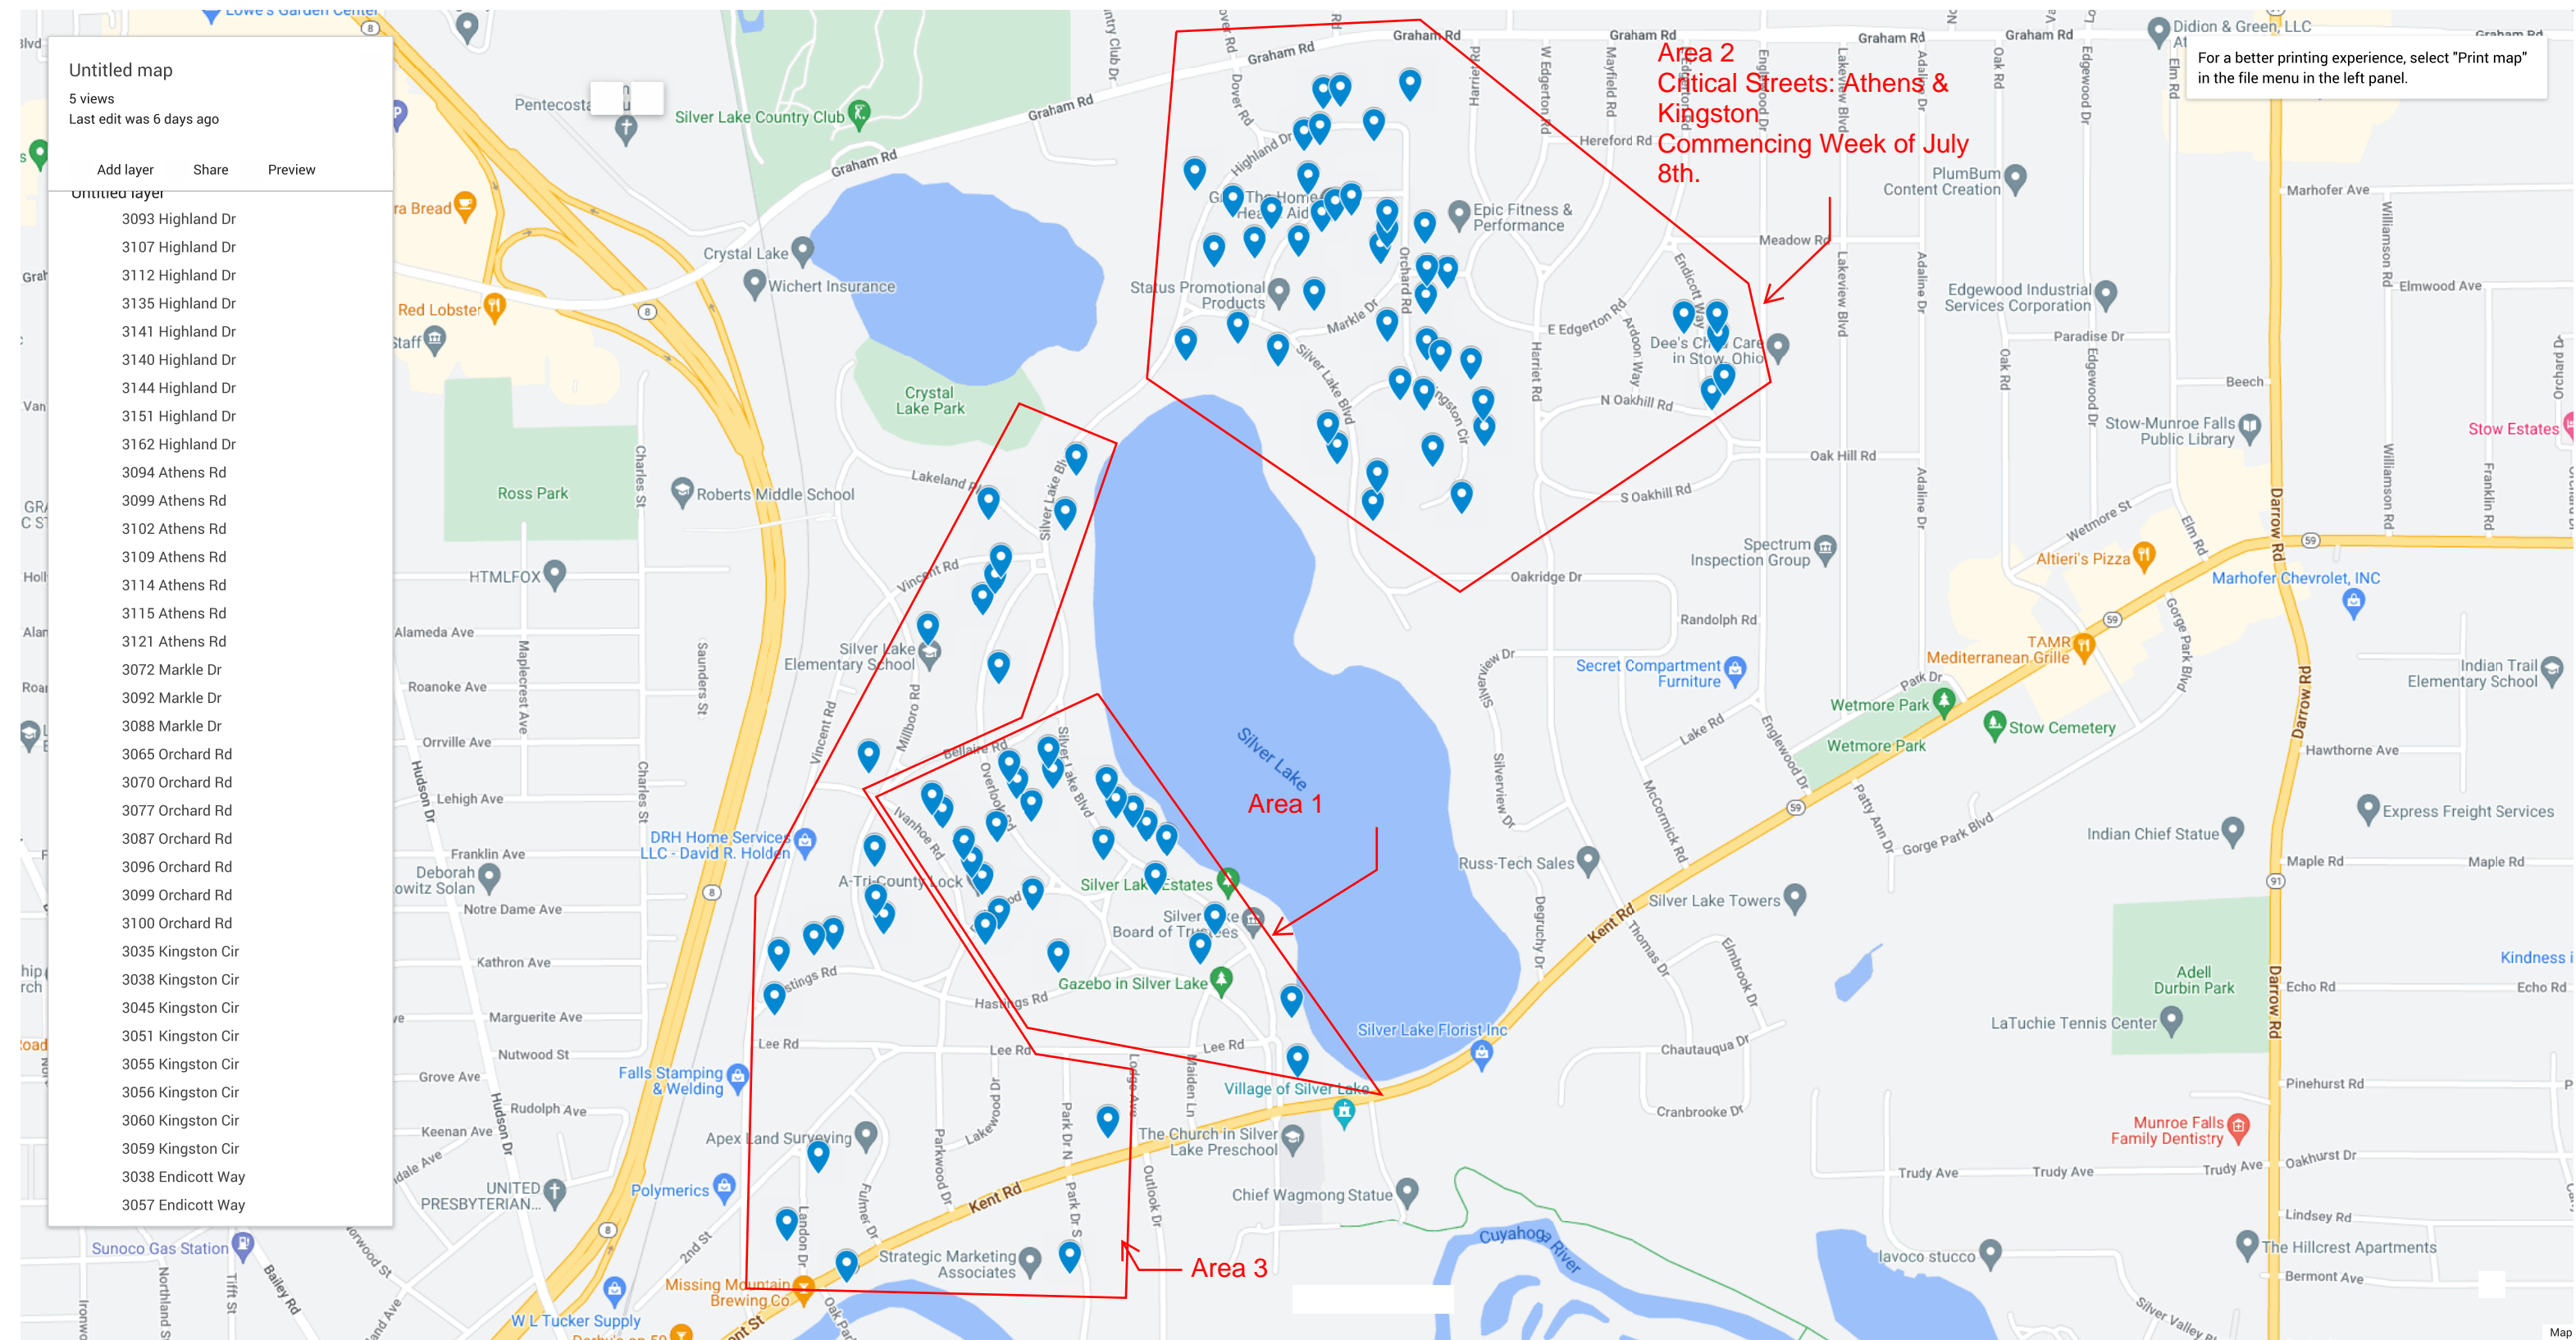

Area 2
Critical Streets: Athens & Kingston
Commencing Week of July 8th.

For a better printing experience, select "Print map" in the file menu in the left panel.
